



Project: Youngstown SMART Network - Preliminary Schedule Date: 10/13/17	Task		External Tasks		Manual Task		Finish-only	
	Split		External Milestone		Duration-only		Deadline	
	Milestone		Inactive Task		Manual Summary Rollup		Progress	
	Summary		Inactive Milestone		Manual Summary			
	Project Summary		Inactive Summary		Start-only			

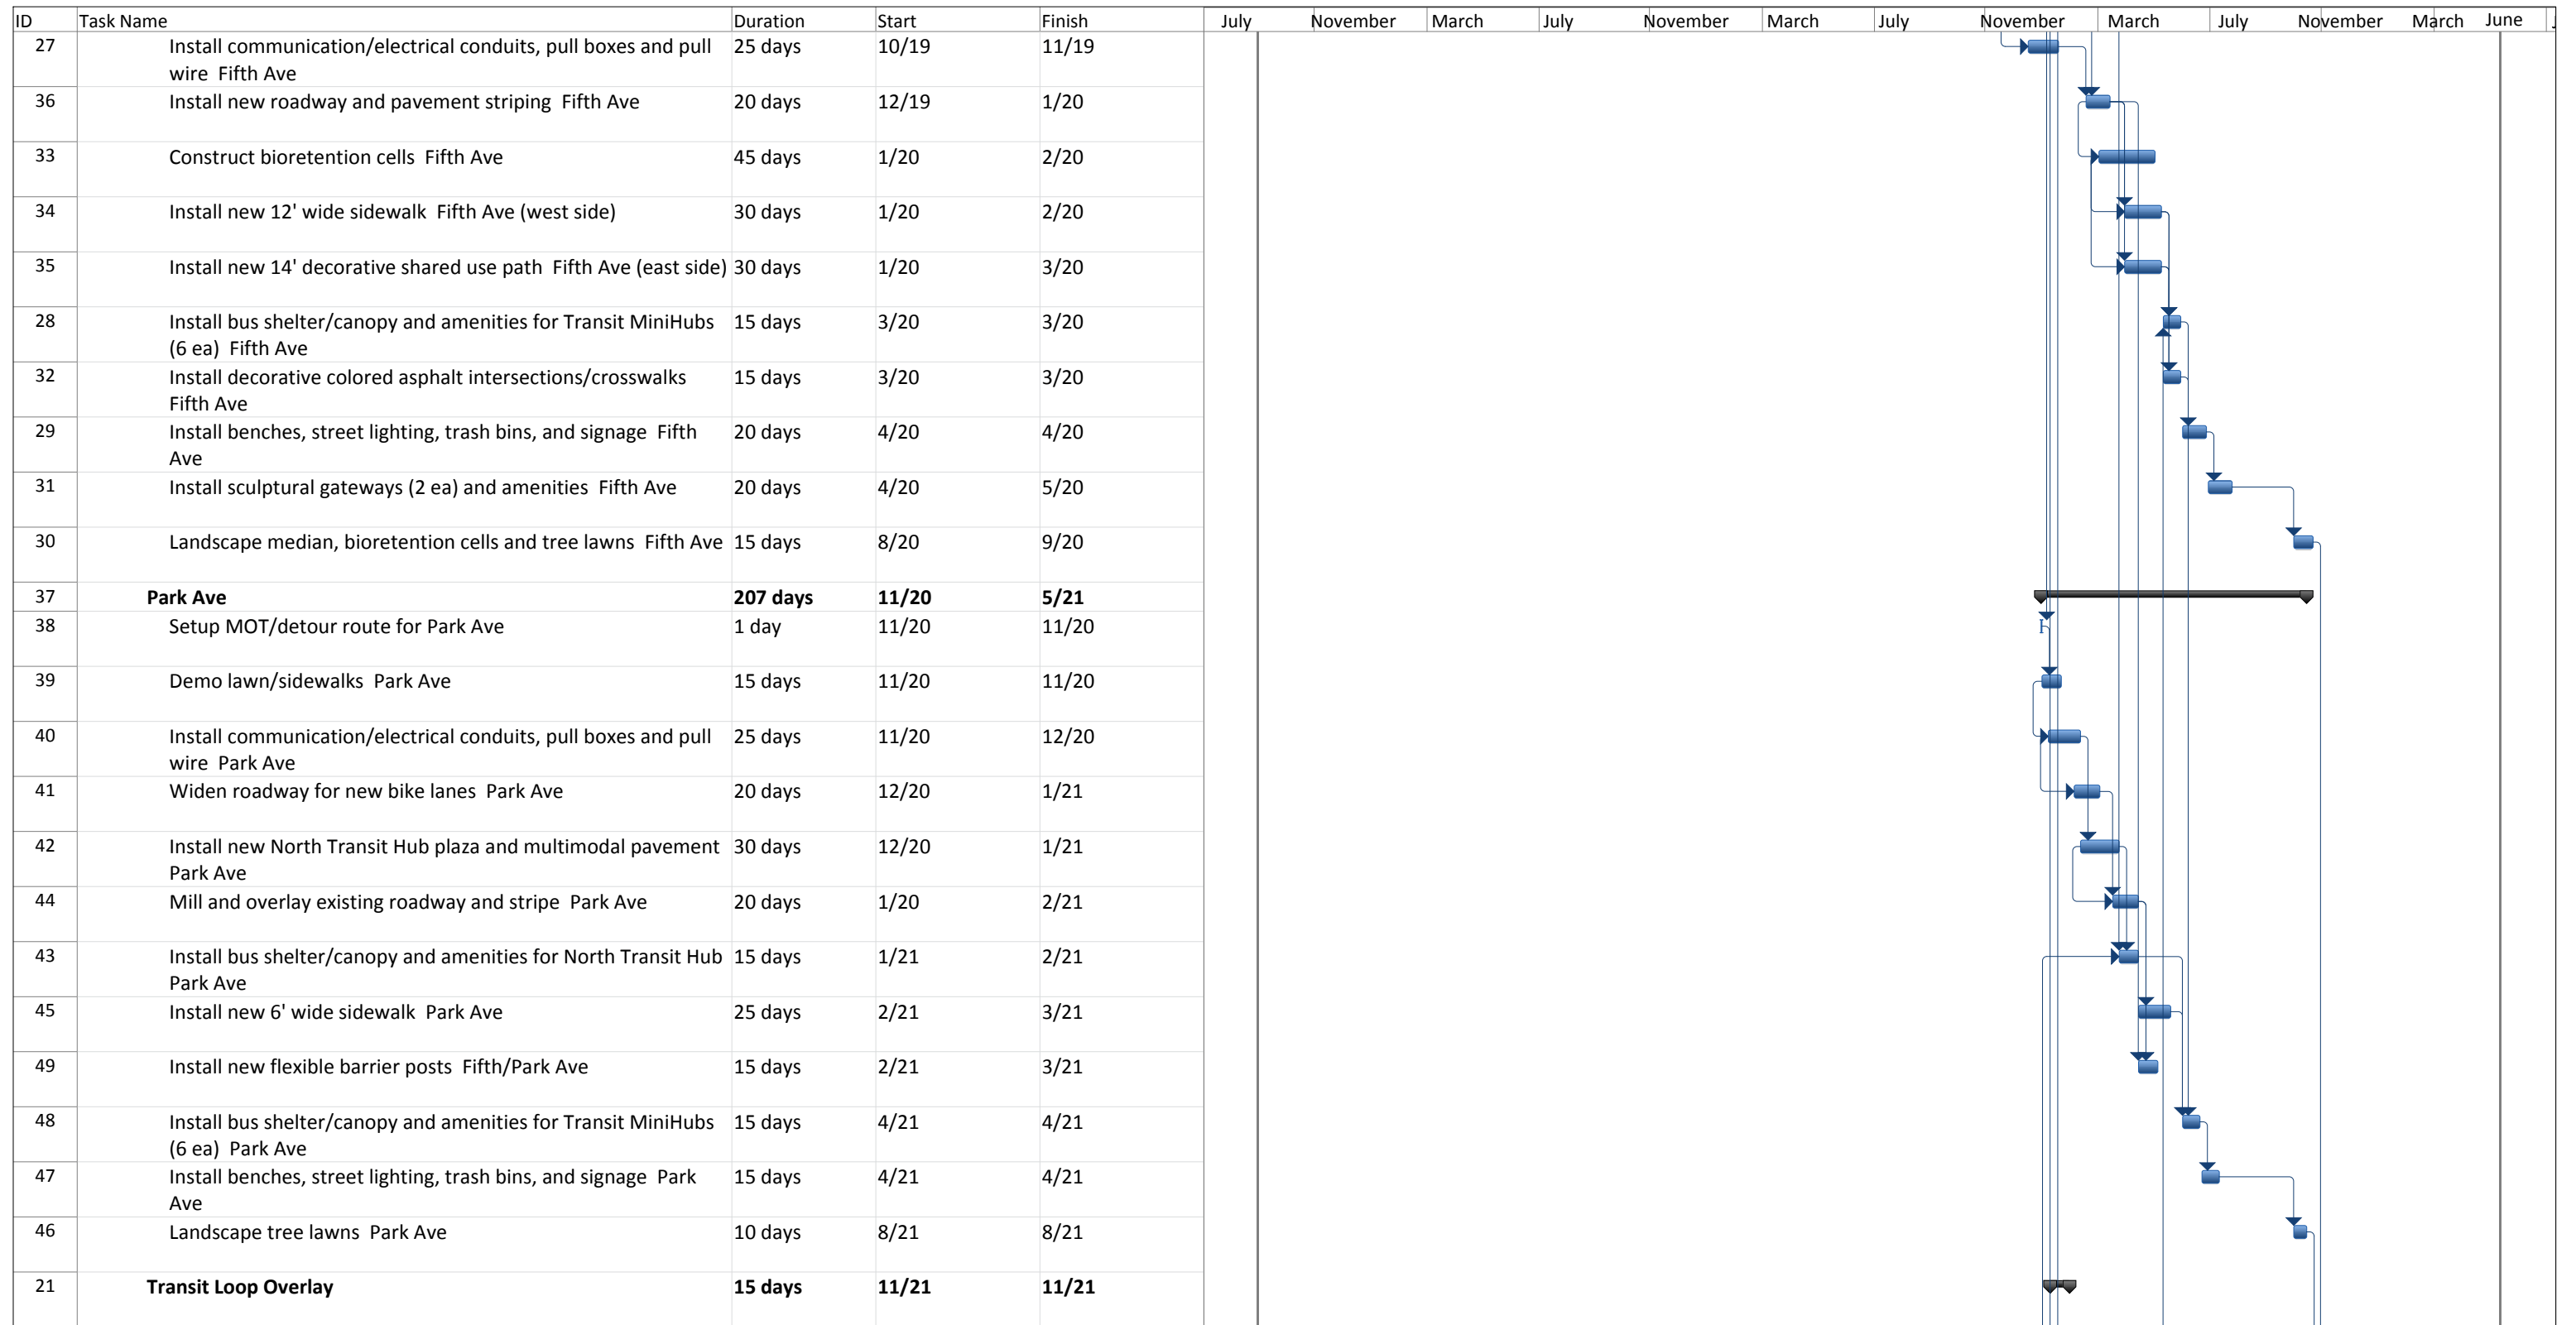

Project: Youngstown SMART Network- Preliminary Schedule Date: 10/13/17	Task		External Tasks		Manual Task		Finish-only	
	Split		External Milestone		Duration-only		Deadline	
	Milestone		Inactive Task		Manual Summary Rollup		Progress	
	Summary		Inactive Milestone		Manual Summary			
	Project Summary		Inactive Summary		Start-only			

ID	Task Name	Duration	Start	Finish	July	November	March	July	November	March	July	November	March	July	November	March	June
22	Install bus shelter/canopy and amenities for Transit MiniHubs (10 ea) Federal Plaza/Walnut St/Rayen Ave	15 days	11/21	11/21													
50	Punch list and systems testing Phase 1	30 days	8/21	9/21													
51	Construction (Summary LOE)	116 days	10/21	6/22													
52	New Bike Lanes	86 days	10/21	1/22													
59	Setup MOT for Mahoning/Tod/West Ave	1 day	10/21	10/21													
53	Remove existing bridge and install new prefab single span steel bridge West Ave	35 days	10/21	11/21													
58	Demo existing lawns and sidewalks Mahoning/Tod/West Ave	15 days	10/21	10/21													
57	Widen roadway for new bike lanes Mahoning/Tod/West Ave	25 days	10/21	11/21													
54	Install new sidewalks, tree lawns, and landscaping Mahoning/Tod/West Ave	30 days	11/21	12/21													
56	Connect new bike lanes to Vallourec bike trail	10 days	11/21	12/21													
55	Pavement striping and install new flexible barrier posts Mahoning/Tod/West Ave	25 days	12/21	1/22													
60	Shared Use Path to Amphitheater	71 days	10/21	2/22													
61	Setup MOT for Spring Commons intersection, MLK Blvd, Front St	1 day	10/21	10/21													
62	Demo for new path and reconfigure Spring Commons, MLK Blvd, Front St	20 days	10/21	11/21													
63	Install new 14' decorative shared use path Fifth Ave to Hazel St	20 days	11/21	12/21													
64	Install benches, lights, bike racks along shared use path Fifth Ave to Hazel St	20 days	12/21	1/22													
65	Connect 14' shared use path to new ped promenade at amphitheater site	10 days	1/22	2/22													
66	Punch list and systems testing	30 days	2/22	6/22													



Project: Youngstown SMART Network - Preliminary Schedule Date: 10/13/17	Task		External Tasks		Manual Task		Finish-only	
	Split		External Milestone		Duration-only		Deadline	
	Milestone		Inactive Task		Manual Summary Rollup		Progress	
	Summary		Inactive Milestone		Manual Summary			
	Project Summary		Inactive Summary		Start-only			
